

Programme Guidelines

for


Intensive Family Food

Production

and

Rainwater

Harvesting

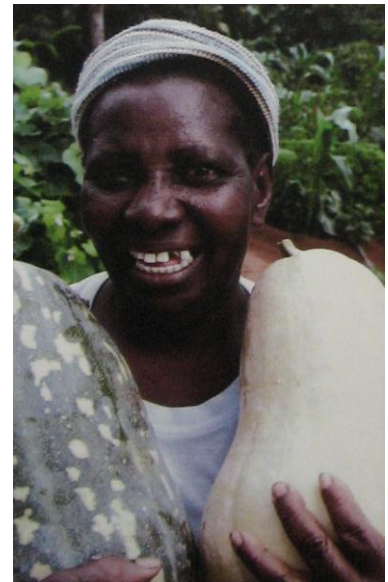

Acknowledgements

The development of policy through which the Department of Water Affairs and Forestry (DWAF) now can actively provide water and the necessary support to enable “productive water uses by the poor”, has a history which has enjoyed the encouragement and understanding of three successive Ministers of Water Affairs, namely former Minister Ronnie Kasrils, former Minister Buyelwa Sonjica and now, the current Minister Lindiwe Hendricks. This is a pro-poor policy which has already proven its potential to impact the poorest households in our society in a very direct, tangible and immediate way.

These Guidelines were drafted on instruction of Mr Tshilidzi Mathobo, DWAF Manager: Agricultural Water Use Development Support, in preparation for full-scale implementation of the DWAF RWH Programme. The Guidelines are based on practical experience gained during the implementation and programme management of the DWAF Rainwater Harvesting Pilot Programme. The following Approved Legal Entities worked directly with poor households in four provinces during the pilot programme, and contributed a significant amount of unpaid time, effort and expense to assist in the development of these Guidelines:

- ❖ LIMA
- ❖ Mvula Trust
- ❖ Rural Integrated Engineering
- ❖ Umhlaba Consulting Group

The DWAF RWH Core Team was responsible for the drafting of these Guidelines, and consisted of members from the following organisations:

- ❖ Socio-Technical Interfacing (coordinating)
- ❖ Border Rural Committee
- ❖ Dams for Africa
- ❖ Mahlatini Organic Seed
- ❖ Makhetha Development Consultancy

MaTshepo Khumbane worked with the Core Team in her personal capacity, and an effort has been made to capture in these Guidelines at least some of the wealth of experience, insights and techniques that she has developed over four decades of dedicated service to our rural poor.

Neither the policy, nor the DWAF RWH programme would have materialised, were it not for the cry of ordinary rural women for “War on Hunger” during the World Summit on Sustainable Development in Johannesburg in 2002. These women took up their picks and shovels and demonstrated in their own backyards what they felt their government had to do to help poor rural women like themselves. These pioneers made their own ‘dams’ and they started growing food in abundance on small patches, they succeeded in their “War on Hunger”, because as they say: “we buried the hunger” – by digging the dams and digging these highly productive trench gardens.

These Guidelines are meant as a tool in the next step of that “War on Hunger” – to help poor rural women catch water where it falls, and use it to send strong healthy children into a bright future of learning and fulfilment.

[Front page: MaTshepo Khumbane, “Hope of the destitute”, ‘The Star’, 28 Feb 2003. Photo: Courtesy ‘The Star’]

Contents

<i>Acknowledgements</i>	ii
<i>Contents</i>	iii
<i>Acronyms</i>	vii
CHAPTER 1 - INTRODUCTION	1
TARGETING FOR MILLENNIUM DEVELOPMENT GOAL 1(A): EXTREME HUNGER.....	1
Where do the Millennium Development Goals come from?.....	1
Do we really have a problem with achieving MDG1(a) in South Africa?.....	1
Does child nutrition really matter?.....	2
The problem in South Africa.....	2
HOW CAN WATER HELP TO ACHIEVE MDG1(A)?.....	3
What is the DWAF RWH Program?.....	3
Does it work?.....	3
CHAPTER 2 - HOW DOES THE DWAF RWH PROGRAM WORK?	5
RULES OF THE GAME.....	7
Working directly with food insecure households.....	7
Working through Registered Implementing Agents (RIAs).....	7
Feasibility Study and Project Implementation Plan.....	7
DWAF/RIA Standard Contract.....	8
Project Implementation.....	8
Invoicing and Payment Processes.....	8
DWAF Monitoring and Evaluation.....	10
CHAPTER 3 - PROJECT IMPLEMENTATION GUIDELINES	11
PROJECT IMPLEMENTATION STAGE.....	11
BACKGROUND.....	12
PROJECT IMPLEMENTATION.....	13
<i>RIA implementation team: overview of functions and staff</i>	13
<i>Organisational set-up</i>	14
a) RIA staff.....	15
b) Site staff from the community.....	16
<i>Roles and Responsibilities of the ISD, FFP and TECH sections</i>	17
<i>Standard Procedures for key implementation activities at Community Level</i>	18
<i>Books and Forms per team position</i>	19
<i>Reporting to the Funding Client</i>	20
<i>RIA's In-house Monitoring and Evaluation</i>	20
PROJECT COMPLETION STAGE.....	20
CHAPTER 4 - FACILITATION PROCESSES FOR COMMUNITIES AND INDIVIDUALS	21
OVERVIEW OF COMMUNITY AND INDIVIDUAL FACILITATION PROCESSES.....	21
CHAPTER 5 - INTRODUCING INTENSIVE FAMILY FOOD PRODUCTION (FFP)	24
OVERVIEW OF FFP FACILITATION PROCESSES.....	24
FFP INTRODUCTION FOR HOUSEHOLDS.....	24
PREPARING FFP FACILITATORS.....	25
DEBRIEFING AND GUIDING FFP FACILITATORS.....	26
FFP STAFF COLLABORATION WITH ISD AND TECH	26

CHAPTER 6 - RWH DAM CONSTRUCTION.....	28
INTRODUCTION.....	28
<i>Preparation at the household level.....</i>	28
<i>Construction process – from the household’s point of view.....</i>	28
<i>Preparation of implementation teams: roles and reporting.....</i>	29
STANDARD RWH DAM.....	29
<i>RWH Dam structure.....</i>	29
Recommended size, shape and elevation.....	29
Standard RWH Dam.....	31
Alternative Designs.....	32
<i>Inlet and overflow structures.....</i>	33
Standard Inlet Structure.....	35
Standard Overflow Structure.....	36
<i>Structural and component design routines.....</i>	37
CONSTRUCTION TOOLS AND EQUIPMENT.....	38
CONSTRUCTION PROCESS.....	38
<i>Dam siting.....</i>	38
<i>Excavation.....</i>	39
<i>Construction.....</i>	40
<i>Quality Assurance.....</i>	42
<i>RWH Dam Testing and Commissioning.....</i>	43
ANCILLARY EQUIPMENT.....	44
<i>Pumping.....</i>	44
REFERENCES.....	45

APPENDICES.....	- 1 -
APPENDIX A: WAR ON HUNGER.....	- 3 -
Does it work?.....	- 5 -
<i>An unexpected way out – “in my own four corners”.....</i>	- 5 -
<i>The plight of many.....</i>	- 7 -
<i>“War on Hunger” – The evolution of a bottom-up policy.....</i>	- 8 -
<i>The cost and value of the DWAF intervention.....</i>	- 10 -
<i>What is intensive Family Food Production and Rainwater Harvesting?.....</i>	- 14 -
<i>Victory in the first battle – Demonstration Phase outcomes.....</i>	- 15 -
<i>Key lessons learnt in the Demonstration Phase.....</i>	- 19 -
<i>Weaponry for the ‘War on Hunger’ – planning for expansion.....</i>	- 20 -
<i>Missing weapons in the armoury.....</i>	- 20 -
<i>RWH and intensive family food production: “What it is” and “what it’s not”.....</i>	- 21 -
APPENDIX B: PROGRAMME DOCUMENTS.....	- 22 -
APPENDIX B1. DWAF PROGRAMME FORMS.....	- 23 -
B1.1 DWAF Call for Expression of Interest: Advertisement.....	- 23 -
B1.2 Application for approval as Registered Implementing Agent (RIA).....	- 24 -
B1.3 Application for DWAF financial assistance for a RWH Feasibility Study.....	- 27 -
B1.4 Application for DWAF financial assistance for a RWH Project.....	- 33 -
APPENDIX B2. PROJECT IMPLEMENTATION PLAN FORMAT.....	- 39 -
APPENDIX B3. PHYSICAL PLANNING ASPECTS.....	- 45 -

APPENDIX B4. RIA BUDGET AND CASH FLOW FORMATS.....	- 51 -
B4.1 Project Budget Summary format.....	- 51 -
B4.2 Invoicing Schedule format	- 52 -
APPENDIX B5. RIA REPORTING & INVOICING FORMATS.....	- 53 -
B5.1 Bi-Monthly Progress Report format	- 53 -
B5.2 Invoicing format.....	- 54 -
APPENDIX C: PROJECT IMPLEMENTATION TOOLS	- 55 -
APPENDIX C1. PROCEDURES.....	- 55 -
C1.1 Procedures for electing PSC and appointing site staff.....	- 56 -
C1.2 Combined Procedures for ISD, FFP and TECH staff.....	- 57 -
C1.3 Procedures for introducing FFP at household level.....	- 58 -
C1.4 Procedures for buying materials.....	- 60 -
C1.5 Procedures for paying wages and salaries	- 61 -
APPENDIX C2. FUNCTIONS OF SITE STAFF	- 62 -
C2.1 Duties of the Bookkeeper	- 63 -
C2.2 Duties of the FFP Assistant	- 66 -
C2.3 Duties of the Storekeeper.....	- 68 -
C2.4 Functions of the Quality Assessor.....	- 69 -
APPENDIX C3. BOOKS AND FORMS	- 71 -
C3.1 Stakeholder contract.....	- 72 -
C3.2 Letter of Appointment	- 75 -
C3.3 Books and Forms used by the Bookkeeper.....	- 76 -
C3.4 Books and Forms used by the FFP Facilitator and FFP Assistant	- 87 -
C3.5 Books and Forms used by the Storekeeper	- 98 -
C3.6 Books and Forms used by the Quality Assessor and QA Assistant	- 105 -
APPENDIX D: FACILITATION PROCESSES.....	- 113 -
APPENDIX D1. DETAILED TABLE: COMMUNITY AND INDIVIDUAL FACILITATION PROCESSES	- 113 -
D1.1 VILLAGE LEVEL FACILITATION PROCESSES	- 121 -
D1.1.1 Introducing the idea of intensive Family Food Production to the community.....	- 121 -
D2.1 INDIVIDUAL MIND MOBILISATION PROCESSES	- 122 -
D2.1.1 Mind mobilisation: introduction	- 122 -
D2.1.2 Household present situation analysis	- 123 -
D2.1.3 Visioning ('Helicopter planning').....	- 124 -
APPENDIX E: FAMILY FOOD PRODUCTION FACILITATION TOOLS	- 125 -
APPENDIX E1. FAMILY FOOD PRODUCTION WORKSHOPS	- 126 -
APPENDIX F: TECHNICAL AND CONSTRUCTION	- 131 -
APPENDIX F1. STANDARD RWH DAM: DRAWINGS.....	- 132 -
APPENDIX F2. WORKSHOP DRAWINGS FOR 'CENTRAL POLE & RADIAL ARM'	- 147 -
APPENDIX F3. STANDARD RWH DAM: SPECIFICATIONS.....	- 158 -
1. Introduction.....	- 158 -
2. Excavation	- 158 -
3. Floor.....	- 159 -
4. Walls	- 160 -
5. Roof Poles.....	- 162 -
6. Waterproofing.....	- 162 -
7. Inlet Structure	- 163 -
8. Overflow Structure.....	- 163 -
9. Roof Sheeting.....	- 164 -
10. Trap Door.....	- 164 -

APPENDIX F4.	STANDARD RWH DAM: CONSTRUCTION MANUAL	- 165 -
APPENDIX F5.	STANDARD RWH DAM: STEP-BY-STEP ILLUSTRATED CONSTRUCTION SEQUENCE	- 189 -
APPENDIX F6.	STANDARD RWH DAM: CONSTRUCTION TOOLS & EQUIPMENT NEEDED.....	- 190 -
APPENDIX F7.	STANDARD RWH DAM LIST OF CONSUMABLE ITEMS NEEDED.....	- 192 -
APPENDIX F8.	RAINWATER HARVESTING LAYOUT: EXAMPLES	- 193 -
APPENDIX F9.	EXCAVATION CONSIDERATIONS	- 199 -
APPENDIX F10.	RWH DAM SAFETY & MAINTENANCE MANUAL	- 203 -
	<i>Introduction</i>	- 203 -
	<i>F10.1 Daily operational Safety Measures for a RWH Dam</i>	- 204 -
	<i>F10.2 Post-rain Safety & Maintenance Inspection for a RWH Dam</i>	- 205 -
	<i>F10.3 Annual Safety & Maintenance Inspection for a RWH Dam</i>	- 208 -
APPENDIX F11.	ALTERNATIVE RWH DAM DESIGNS	- 213 -
APPENDIX F12.	RWH DAM DESIGN ROUTINES	- 219 -

Acronyms

ALE	Approved Legal Entity
BK	Bookkeeper
DoA	Department of Agriculture
DWAF	Department of Water Affairs and Forestry
EoI	Expression of Interest
FFP	(Intensive) Family Food Production
FFP-A	FFP Assistant
FFP-F	FFP Facilitator
FFP-M	FFP Manager
IRR	Internal Rate of Return
ISD	Institutional and Social Development
ISD-F	ISD Facilitator
ISD-M	ISD Manager
LN-SI	Large Number-Small Infrastructure projects
MDG	Millennium Development Goals
MM	Mind Mobilisation
PSC	Project Steering Committee , consisting of elected community members
PVC pipes	Poly-Vinyl-Chloride pipes
QA	Quality Assessor
QAA	Quality Assessor Assistant
RIA	Registered Implementing Agent
RWH	Rainwater Harvesting
SK	Storekeeper
TECH staff	Technical and construction staff
TO	Technical Officer
VIP toilet	Ventilated Improved Pit toilet
